



Community High School District 99

## Master Facility Plan Implementation

# Bi-Weekly Construction Progress Report

Period: 03/25/21 - 04/07/21


### **Wight Construction Services**

2500 North Frontage Road  
Darien, IL 60561



## Phase C - Auditorium

- Poured Upper Parterre seats, sloped Parterre seats, Orchestra Pit, and Stage Slabs
- Continued installing metal stairs throughout the auditorium box and poured their steps
- Started installing Scene Shop Mezzanine structural steel
- Continued installing door frames as well as drywall, tape, and paint throughout
- Continued piping below stage and completed underground rough-in for parterre and stage areas
- Completed rough-in for cheek wall and vestibules lights
- Started installing return plenum as well as grilles throughout
- Completed tiling west events bathrooms and started framing and rough-ins for East Auditorium Bathrooms. Completed rough-ins for cafe and field measured for kitchen equipments

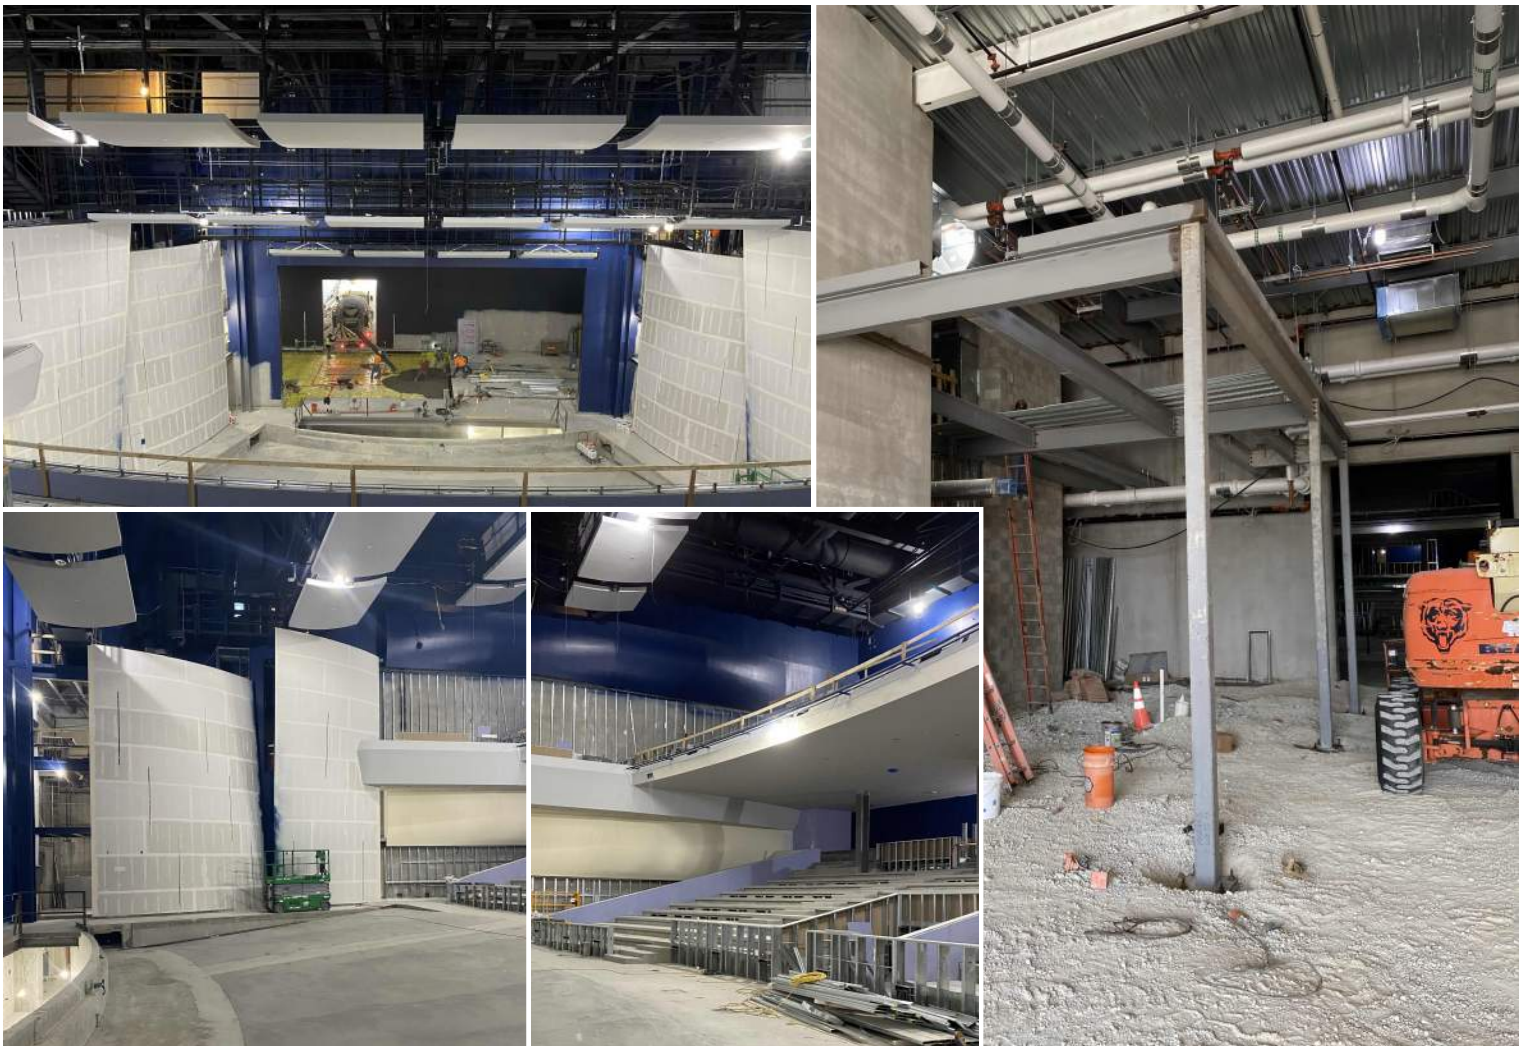

360° Pictures:

[Auditorium Box](#)

[Fly Tower](#)


[Auditorium Balcony](#)

[Scene Shop](#)



## Phase C - Learning Commons & Other Areas

- Completed installing exterior commons curtain wall glazing. Doors will follow
- Installed curtain wall frame and glass for the north commons stairs
- Installed wood panels around commons window frames and interior window trims
- Installed the ceiling grid in the study lofts
- Continued duct installation in commons
- Completed demo of existing IT area, cafeteria ceiling, and first floor offices. Installed new temp access to library and closed down its main entrance
- Abated existing floors in hallways on 2nd and 3rd floors.
- Continued floating 1st floor B hallway to resume tile installation
- Continued installing sprinkler piping across the school. Continued Fire Alarm installations in commons as well as data rough-in

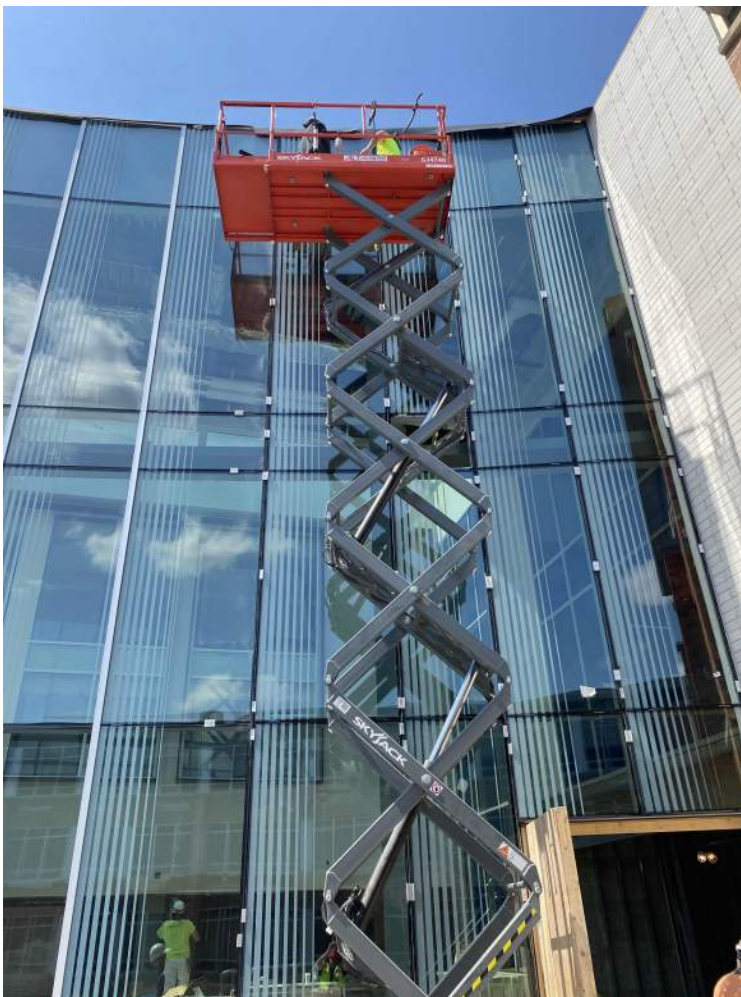

360° Pictures:

[Grand Stairs](#)

[South Commons](#)

[North Commons](#)



## Phase C - Courtyard and Other Areas

- Wooding siding in commons scheduled to be completed this week
- Framing walls and ceiling soffits in café complete
- Currently installing acoustical ceiling grid on 2nd 3rd floor bridge
- Began installing skylight system on west & east sides of commons. Detailing to continue this week while waiting for end break metal to be fabricated
- 3rd floor Breakout rooms glazing to begin next week
- Chiller has been released for fabrication with an estimated delivery of mid June 2021 (Capital 2021)

### Transition Building

- Completed underground plumbing and poured back concrete
- Began installing new water line to back of building and overhead insulation at roof deck
- Began installing metal framing top & bottom track



360° Pictures:

[Commons](#)

[Studio Room](#)

