



Hardscape:

1/6 – 1/10

- Median Sign Foam
- Median Sign Stucco
- Blvd Column Lighting (All columns that had lights previously are working with exception to 3)

1/13 – 1/17


- Median Sign Stucco (Should be completed that week)
- Median Sign Foam (Should be completed that week)
- Troubleshoot lighting
- Install Median Sign lettering (Awaiting Lettering)
- (We are reviewing the submitted cable rail specifications from the manufacturer this week for accuracy)
- (Reviewing Planter manufacturer options this week)
- Small column bore for irrigation sleeve (X4). (Preemptive measure to avoid delay after planters are manufactured)

Landscape & Irrigation:


- Phase 1, 2 and 3 Irrigation and Landscape installation is complete (excluding main entry). Final cleanup to be completed prior to turnover.
- Note: Front Entry Monument Landscape scheduling is pending completion of gas line installation and entry monument painting.
- Irrigation meeting is scheduled for 1/21



Note: Phase 1 Landscape Installation Limit is to location shown on map below.

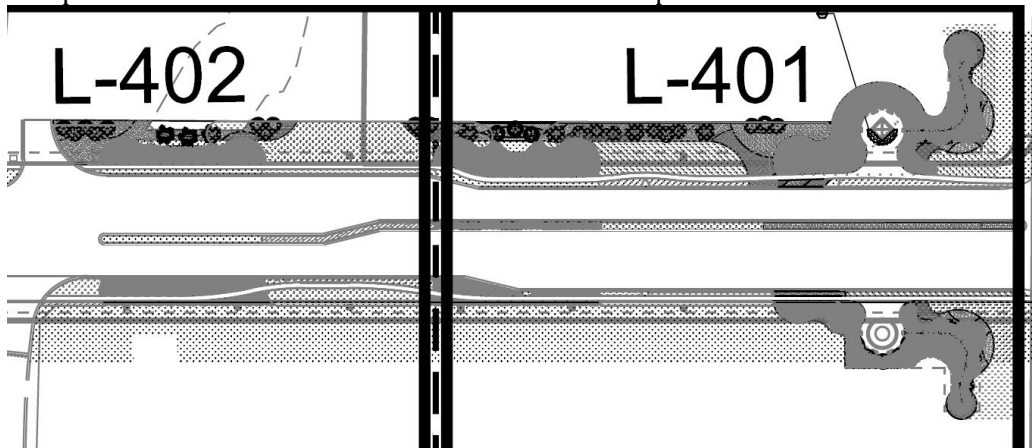

Note: Phase 2 Landscape Installation Limit is to location shown on map below.

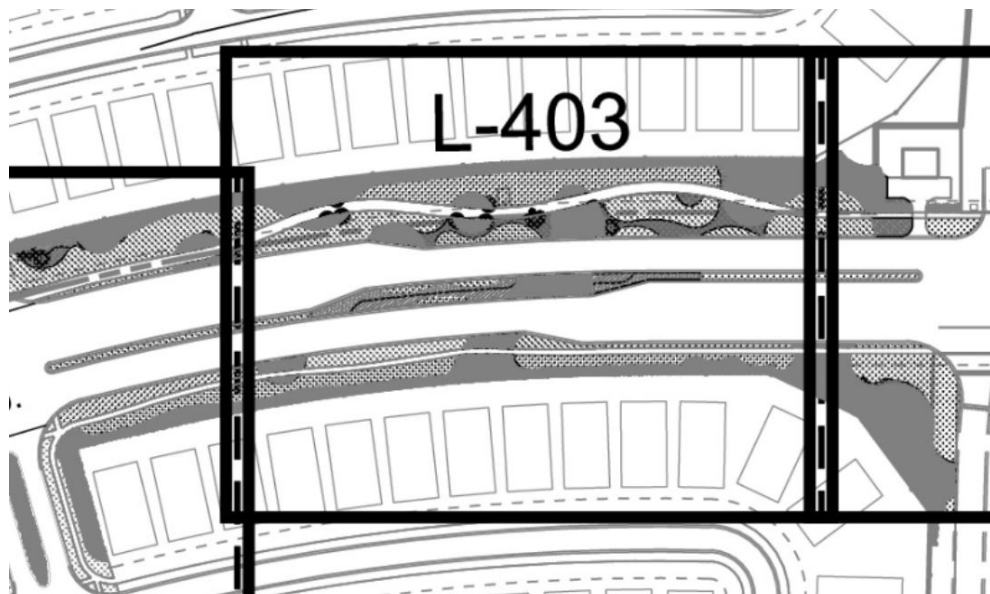



CAPITAL Land Management

Design-Build
Maintenance
Agronomics
Irrigation

Lakeland

Orlando

Tampa

Note: Phase 3 Landscape Installation Limit is to location shown on map below.

