



Hardscape:

Jan 20, 2020 – Jan 24, 2020

- Median Sign stucco touch ups
- Median Sign Painting
- BLVD Column punch out. (We did additional stucco repairs as we found missed spots. Paint Touch up)

Jan 27 – Jan 31


- Median Sign letter installation.
- Start cable rail fencing install. (If delivery is on time)
- Entry sign punch out. (Electrical is ran for the backlighting, installation coming.)

Landscape & Irrigation:


- Phase 1, 2 and 3 Irrigation and Landscape installation is complete (excluding main entry). Final cleanup to be completed prior to turnover. Minor modifications to be adjusted to irrigation system per meeting on 1/21/2020.
- Note: Front Entry Monument Landscape scheduling is pending completion of gas line installation and entry monument painting.
- Irrigation repairs at new Publix entry to be completed pending installation of curbing.



Note: Phase 1 Landscape Installation Limit is to location shown on map below.

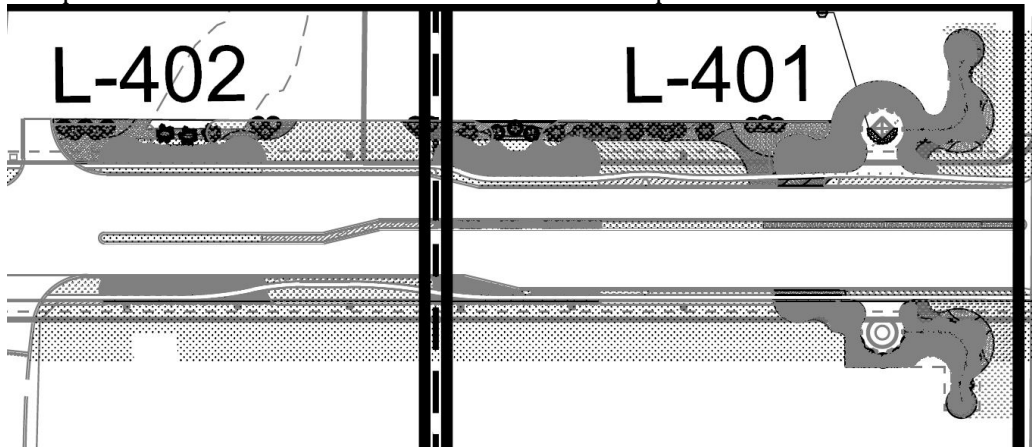

Note: Phase 2 Landscape Installation Limit is to location shown on map below.

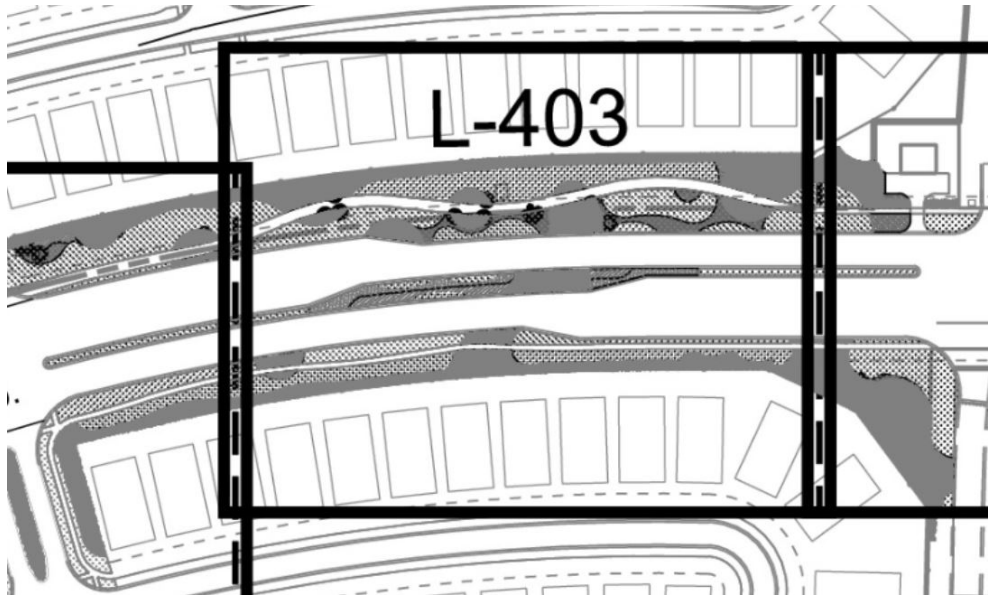



CAPITAL Land Management

Design-Build
Maintenance
Agronomics
Irrigation

Lakeland

Orlando

Tampa

Note: Phase 3 Landscape Installation Limit is to location shown on map below.

